

Draft Confluence Parkway NEPA/SEPA Compliance (FHWA/WSDOT and City of Wenatchee)

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Timeline									
								April 1	October 11	April 21	November 1	May 11	November 21	June 1			
1	→	NEPA/SEPA EIS Coordination and Outreach	260 days	Tue 8/21/18	Thu 8/29/19												
2	→	Core Team Meetings	13 mons	Tue 8/21/18	Thu 8/29/19												
3	→	City/FHWA Coordination Meetings	11.5 mons	Mon 10/1/18	Tue 8/27/19												
4	→	Chelan PUD Coordination Meetings	13 mons	Tue 8/21/18	Thu 8/29/19												
5	→	Public Open House	1 wk	Mon 4/8/19	Fri 4/12/19												
6	→	Stakeholder Coordination Meeting	1 wk	Mon 4/8/19	Fri 4/12/19	5SS											
7	→	NEPA/SEPA Analyses	420.5 days	Mon 2/4/19	Wed 9/30/20												
8	→	FHWA/WSDOT NEPA Document Kick Off Meeting	1 wk	Mon 3/25/19	Fri 3/29/19	14											
9	→	EA Coordination Plan for Agency and Public Involvement	35 days	Mon 2/4/19	Fri 3/22/19												
10	→	Draft EA Coordination Plan, in coordination with FHWA	2 wks	Mon 2/4/19	Fri 2/15/19												
11	→	City Review	1 wk	Mon 2/18/19	Fri 2/22/19	10											
12	→	Revise EA Coordination Plan, in coordination with FHWA	1 wk	Mon 2/25/19	Fri 3/1/19	11											
13	→	FHWA/WSDOT Review	2 wks	Mon 3/4/19	Fri 3/15/19	12											
14	→	Draft Final EA Coordination Plan, FHWA/WSDOT Confirm Lead, Cooperating, and Participating Agencies	1 wk	Mon 3/18/19	Fri 3/22/19	13											
15	→	Formal Project Initiation	25 days	Mon 3/25/19	Sun 4/28/19												
16	→	Invitation Letters Sent to Cooperating and Participating Agencies	1 wk	Mon 3/25/19	Fri 3/29/19	14											
17	→	Confirmation of Cooperating and Participating Agencies	30 edays	Fri 3/29/19	Sun 4/28/19	16											
18	→	Purpose and Need Statement, Range of Alternatives (based on Pre-NEPA Study)	70 days	Mon 2/11/19	Fri 5/17/19												
19	→	Refine P&N (based on FHWA/WSDOT/Core Team Input)	3 wks	Mon 2/11/19	Fri 3/1/19												
20	→	City/FHWA/WSDOT Review	2 wks	Mon 3/4/19	Fri 3/15/19	19											
21	→	Revise P&N	1 wk	Mon 3/18/19	Fri 3/22/19	20											
22	→	Cooperating and Participating Agency Review (overlaps with public outreach meeting)	30 edays	Fri 3/29/19	Sun 4/28/19	21,16											
23	→	Finalize P&N and Range of Alternatives (with City/FHWA/WSDOT Input)	3 wks	Mon 4/29/19	Fri 5/17/19	22,5,6											
24	→	Early Studies and Analyses	115 days	Mon 2/18/19	Wed 7/31/19												
25	→	Alternative draft alignments completed	3 wks	Mon 2/18/19	Fri 3/8/19												
26	→	Alternative draft final alignments completed	2 wks	Mon 5/20/19	Mon 6/3/19	23											
27	→	Visual Analyses (50%)	85 days	Mon 2/18/19	Mon 6/17/19												
28	→	Develop methodology and approach	4 wks	Mon 2/18/19	Fri 3/15/19	25SS											
29	→	Develop visual simulations	2 wks	Mon 3/18/19	Fri 3/29/19	25,28											
30	→	Draft Technical Report	3 wks	Mon 4/1/19	Fri 4/19/19	29											
31	→	City/FHWA/WSDOT Review	2 wks	Mon 4/22/19	Fri 5/3/19	30											
32	→	Finalize Technical Report	2 wks	Tue 6/4/19	Mon 6/17/19	31,26											
33	→	Noise Analyses (50%)	85 days	Mon 2/18/19	Mon 6/17/19												

Project: Confluence Parkway Date: Wed 2/13/19	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only		Manual Progress	
	Summary		Inactive Task		Duration-only		Finish-only			


Draft Confluence Parkway NEPA/SEPA Compliance (FHWA/WSDOT and City of Wenatchee)

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names									
								April 1	October 11	April 21	November 1	May 11	November 21	June 1		
34	→	Develop methodology and approach	4 wks	Mon 2/18/19	Fri 3/15/19	25SS										
35	→	Draft Technical Report	3 wks	Mon 3/18/19	Fri 4/5/19	25,34										
36	→	City/FHWA/WSDOT Review	2 wks	Mon 4/8/19	Fri 4/19/19	35										
37	→	Finalize Technical Report	2 wks	Tue 6/4/19	Mon 6/17/19	36,26										
38	→	Archeological and Historic Technical Report (50%)	85 days	Mon 2/18/19	Mon 6/17/19											
39	→	Develop Study Plan, in coordination with FHWA	3 wks	Mon 2/18/19	Fri 3/8/19	25SS										
40	→	Section 106 Initiation Letters Sent; Consulting Party Review of Study Plan	30 edays	Fri 3/8/19	Sun 4/7/19	39										
41	→	Field Reconnaissance, including preparation and completion	2 wks	Mon 4/8/19	Fri 4/19/19	40										
42	→	Draft Technical Report	3 wks	Mon 4/22/19	Fri 5/10/19	41										
43	→	City/FHWA/WSDOT Review	2 wks	Mon 5/13/19	Fri 5/24/19	42										
44	→	Finalize Technical Report	2 wks	Tue 6/4/19	Mon 6/17/19	43,26										
45	→	Section 4(f) Technical Report (50%)	110 days	Mon 2/18/19	Tue 7/23/19											
46	→	Develop methodology and approach	4 wks	Mon 2/18/19	Fri 3/15/19	25SS										
47	→	Draft Technical Report	3 wks	Tue 6/4/19	Mon 6/24/19	29,35,42,26										
48	→	City/FHWA/WSDOT Review	2 wks	Tue 6/25/19	Tue 7/9/19	47										
49	→	Finalize Technical Report	2 wks	Wed 7/10/19	Tue 7/23/19	48										
50	→	Additional Preliminary NEPA Analyses (Based on NEPA CE Form)	40 days	Mon 2/18/19	Fri 4/12/19											
51	→	Review Additional Elements of the Environment	4 wks	Mon 2/18/19	Fri 3/15/19	25SS										
52	→	Confirm Nonsignificance/Significance with FHWA/WSDOT	2 wks	Mon 3/18/19	Fri 3/29/19	51										
53	→	Identify Additional Studies (if needed)	2 wks	Mon 4/1/19	Fri 4/12/19	52										
54	→	Additional Funding Received	0 days	Wed 7/31/19	Wed 7/31/19											
55	→	Draft NEPA EA/SEPA Checklist	300.5 days	Tue 7/23/19	Wed 9/30/20											
56	→	FHWA/WSDOT Confirm EA v EIS	0 days	Tue 7/23/19	Tue 7/23/19	32,37,44,49,52										
57	→	Draft NEPA EA/SEPA Checklist	300.5 days	Wed 7/24/19	Wed 9/30/20											
58	→	FHWA/WSDOT/City Confirm Alternative(s)	2 wks	Wed 7/24/19	Tue 8/6/19	56										
59	→	Technical Studies Methodologies	57 days	Wed 8/7/19	Fri 10/25/19											
60	→	Develop methodology and impact analysis approach	2 wks	Wed 8/7/19	Tue 8/20/19	56,58										
61	→	City/FHWA/WSDOT Review	2 wks	Wed 8/21/19	Wed 9/4/19	60										
62	→	Revise methodology and impact analysis approach	1 wk	Thu 9/5/19	Wed 9/11/19	61										
63	→	Cooperating and Participating Agency Review	30 edays	Wed 9/11/19	Fri 10/11/19	62										
64	→	Finalize methodology and impact analysis approach	2 wks	Mon 10/14/19	Fri 10/25/19	63										
65	→	Technical Studies Preparation	80 days	Mon 10/28/19	Tue 2/25/20											
66	→	Archeological and Historic Technical Report (Section 106)	4 mons	Mon 10/28/19	Tue 2/25/20	64										

Project: Confluence Parkway Date: Wed 2/13/19	Task Project Summary Split External Tasks Milestone External Milestone Summary Inactive Task	Inactive Milestone Inactive Summary Manual Task Duration-only	Manual Summary Rollup Manual Summary Start-only Finish-only	Deadline Progress Manual Progress
--	---	--	--	---

Draft Confluence Parkway NEPA/SEPA Compliance (FHWA/WSDOT and City of Wenatchee)

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Timeline						
								April 1	October 11	April 21	November 1	May 11	November 21	June 1
67	→	Section 4(f) Technical Report	4 mons	Mon 10/28/19	Tue 2/25/20	64								
68	→	Biological Assessment	4 mons	Mon 10/28/19	Tue 2/25/20	64								
69	→	Draft EA Preparation	140 days	Mon 10/28/19	Tue 5/19/20									
70	→	Prepare Draft EA	5 mons	Mon 10/28/19	Tue 3/24/20	58,64								
71	→	FHWA/WSDOT/City Review	3 wks	Wed 3/25/20	Tue 4/14/20	70								
72	→	Revise Draft EA	2 wks	Wed 4/15/20	Tue 4/28/20	71								
73	→	Cooperating and Participating Agency Preview (Meeting)	1 wk	Wed 4/29/20	Tue 5/5/20	72								
74	→	Finalize and Publish Draft EA	2 wks	Wed 5/6/20	Tue 5/19/20	73								
75	→	Draft EA Public Review Process	30 edays	Tue 5/19/20	Thu 6/18/20	74								
76	→	Final EA Preparation	62.5 days	Fri 6/19/20	Wed 9/16/20									
77	→	Review Public Comments	2 wks	Fri 6/19/20	Thu 7/2/20	75								
78	→	Prepare Final EA	1 mon	Fri 7/10/20	Thu 8/6/20	77,87,88,89								
79	→	FHWA/WSDOT/City Review	3 wks	Fri 8/7/20	Thu 8/27/20	78								
80	→	Finalize EA	2.5 wks	Fri 8/28/20	Wed 9/16/20	79								
81	→	FHWA Publish Final EA and FONSI	0 days	Thu 9/17/20	Thu 9/17/20	80FS+1 day								
82	→	Complete SEPA Checklist/City Issue DNS	0 days	Wed 9/16/20	Wed 9/16/20	80FF								
83	→	Public Notice of FONSI and DNS	14 edays	Wed 9/16/20	Wed 9/30/20	82								
84	→	Environmental Approvals and Permits	221 days	Tue 2/25/20	Fri 1/8/21									
85	→	Application Preparation/Submittal	1 mon	Fri 8/28/20	Fri 9/25/20	79								
86	→	Federal	144.5 days	Tue 2/25/20	Thu 9/17/20									
87	→	ESA/EFH Consultation, Bald and Golden Eagle Approvals Completed	135 edays	Tue 2/25/20	Thu 7/9/20	68								
88	→	Section 106 Consultation and Native American Graves Protection Act Completed	4.5 mons	Wed 2/26/20	Wed 7/1/20	66								
89	→	Section 4(f) Determination	4.5 mons	Wed 2/26/20	Wed 7/1/20	67								
90	→	Section 10/404 Permit, Migratory Bird Treaty Act Compliance	1 mon	Wed 8/19/20	Thu 9/17/20	87,88,81FF								
91	→	Bridge Permit Issued	1 mon	Wed 8/19/20	Thu 9/17/20	81FF,87,88								
92	→	State	76.5 days	Thu 9/17/20	Fri 1/8/21									
93	→	Section 402 NPDES	45 edays	Fri 9/25/20	Mon 11/9/20	85,82								
94	→	401 Water Quality Certification	0 days	Thu 9/17/20	Thu 9/17/20	90FF								
95	→	Hydraulic Project Approval (?)	45 edays	Fri 9/25/20	Mon 11/9/20	85,82								
96	→	DNR AUA (?)	2 wks	Thu 12/24/20	Fri 1/8/21	90,91,93,94,95								
97	→	Local	60 days	Mon 9/28/20	Wed 12/23/20									
98	→	SSDP	3 mons	Mon 9/28/20	Wed 12/23/20	85,82								

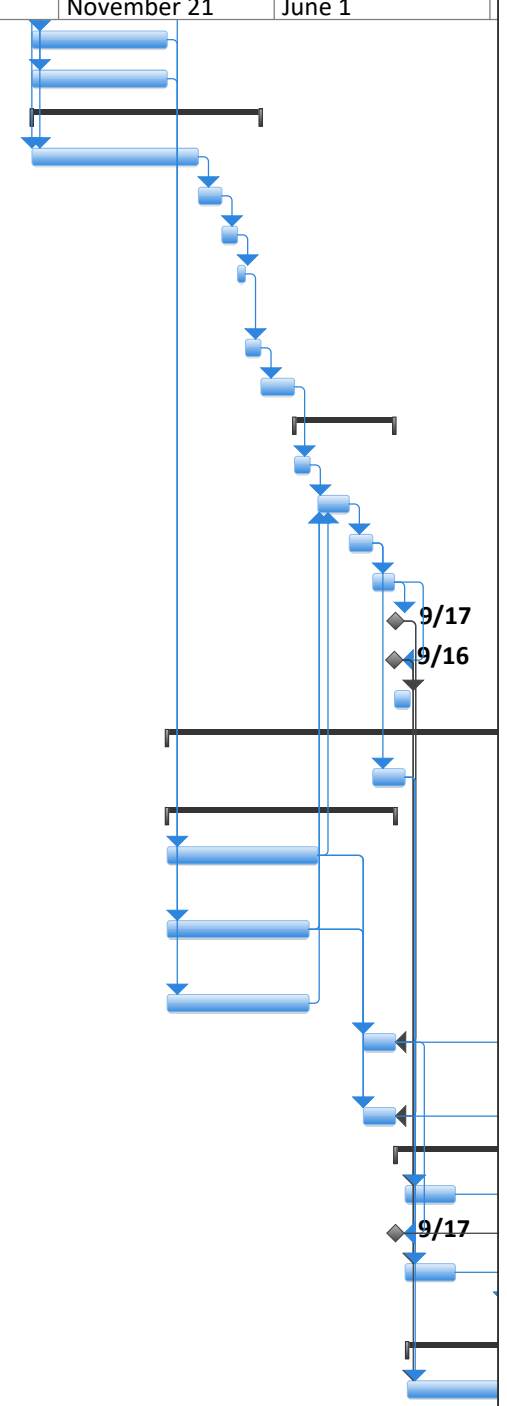

Project: Confluence Parkway Date: Wed 2/13/19	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only		Manual Progress	
	Summary		Inactive Task		Duration-only		Finish-only			
